4. Minimax and planning problems

- Optimizing piecewise linear functions
- Minimax problems
- Example: Chebyshev center
- Multi-period planning problems
- Example: building a house

Linear programs have polyhedral feasible sets:

$$\{x \mid Ax \leq b\} \Longrightarrow$$



Can every polyhedron be expressed as $Ax \le b$?


Not this one...



If $x, y \in \mathbb{R}^n$, then the linear combination

$$w = \alpha x + (1 - \alpha)y$$
 for some $0 \le \alpha \le 1$

is called a **convex combination**. As we vary α , it traces out the line segment that connects x and y.



If $Ax \le b$ and $Ay \le b$, and w is a convex combination of x and y, then $Aw \le b$.

Proof: Suppose
$$w = \alpha x + (1 - \alpha)y$$
.

$$Aw = A(\alpha x + (1 - \alpha)y)$$

$$= \alpha Ax + (1 - \alpha)Ay$$

$$\leq \alpha b + (1 - \alpha)b$$

$$= b$$

Therefore, $Aw \leq b$, which is what we were trying to prove.

Question: where did we use the fact that $0 \le \alpha \le 1$?

The previous result implies that every polyhedron describable as $Ax \le b$ must contain all convex combinations of its points.

- Such polyhedra are called convex.
- Informal definition: if you were to "shrink-wrap" it, the entire polyhedron would be covered with no extra space.

Convex:



Not convex:




Goes the other way too: every convex polyhedron can be represented as $Ax \le b$ for appropriately chosen A and b.

- Some problems do not appear to be LPs but can be converted to LPs using a suitable transformation.
- An important case: convex piecewise linear functions.


Consider the following **nonlinear** optimization:


minimize
$$f(x)$$
 subject to: $x \ge 0$

Where f(x) is the function:



The trick is to convert the problem into **epigraph** form: add an extra decision variable *t* and turn the cost into a constraint!

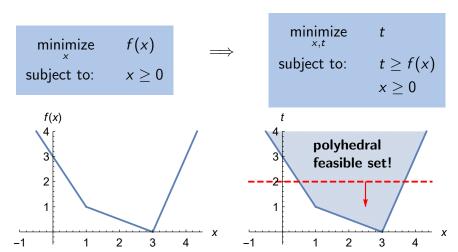



$\mathop{minimize}_{x,t}$	t
subject to:	$t \ge f(x)$ $x \ge 0$


This feasible set is **polyhedral**. It is the set of (x, t) satisfying:

$$\{t \ge -2x + 3, \quad t \ge -\frac{1}{2}x + \frac{3}{2}, \quad t \ge 3x - 9\}$$

Equivalent linear program:

minimize
$$t$$
 subject to: $t \ge -2x + 3, \quad t \ge -\frac{1}{2}x + \frac{3}{2}$ $t \ge 3x - 9, \quad x \ge 0$

Epigraph trick only works if it's a convex polyhedron.





This epigraph is **not** a **convex polyhedron** so it cannot be the feasible set of a linear program.

Minimax problems

The maximum of several linear functions is always convex.
 So we can minimize it using the epigraph trick. Example:

$$f(x) = \max_{i=1,\dots,k} \left\{ a_i^\mathsf{T} x + b_i \right\}$$





 $\min_{x} \max_{i=1,\dots,k} \left\{ a_i^\mathsf{T} x + b_i \right\}$

 \Longrightarrow


 $\min_{x,t} t$


s.t. $t \geq a_i^\mathsf{T} x + b_i \quad \forall$

Maximin problems

• The minimum of several linear functions is *always* concave. So we can maximize it using the epigraph trick. Example:

$$f(x) = \min_{i=1,\dots,k} \left\{ a_i^\mathsf{T} x + b_i \right\}$$





 $\max_{x} \min_{i=1,...,k} \left\{ a_i^\mathsf{T} x + b_i \right\}$

 \Longrightarrow

 $\max_{x,t} t$ s.t. $t < a_i^T x + b_i \forall i$

Minimax and Maximin problems

A minimax problem:

$$\min_{x} \max_{i=1,\dots,k} \left\{ a_i^\mathsf{T} x + b_i \right\} \qquad \Longrightarrow \qquad \min_{x,t} \quad t \\
\text{s.t.} \quad t \ge a_i^\mathsf{T} x + b_i \quad \forall i$$

A maximin problem:

$$\max_{x} \min_{i=1,\dots,k} \left\{ a_i^{\mathsf{T}} x + b_i \right\} \qquad \Longrightarrow \qquad \max_{x,t} \quad t$$

$$\mathrm{s.t.} \quad t \leq a_i^{\mathsf{T}} x + b_i \quad \forall i$$

Note: Sometimes called *minmax*, *min-max*, *min/max*. Of course, minmax \neq maxmin!

Minimax and Maximin problems

Practical scenario:

- Paintco produces specialized paints and we are planning production for the coming year. They have some flexibility in how they produce the paints, but ultimately they require employees, as well as electricity, water, and certain chemicals.
- Nobody knows for sure how much paints will sell for, and the future price of electricity, water, and the chemicals is also unknown. But planning decision must be made now.
- Three consulting firms are hired to forecast the costs for the coming year. The three firms return with three different forecasts (cost functions f_1 , f_2 , f_3). Which one should be used?
- The risk-averse approach is to solve the minimax problem:

$$\min_{x} \max_{i=1,2,3} \{ f_i(x) \} \neq \max_{i=1,2,3} \{ \min_{x} f_i(x) \}$$

Absolute values

Absolute values are piecewise linear!




So are sums of absolute values:

$$\min_{x,y} |x| + |y| \qquad \Longrightarrow \qquad \min_{x,y,t,r} t + r$$

$$\text{s.t.} \quad t \ge x, \quad t \ge -x$$

$$r \ge y, \quad r \ge -y$$

What is the largest sphere you can fit inside a polyhedron?

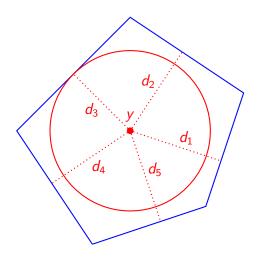


If *y* is the center, then draw perpendicular lines to each face of the polyhedron.

We want to maximize the smallest d_i . In other words,

$$\max_{y} \min_{i=1,\dots,5} \frac{d_i(y)}{d_i(y)}$$

(the *y* shown here is obviously not optimal!)

What is the largest sphere you can fit inside a polyhedron?

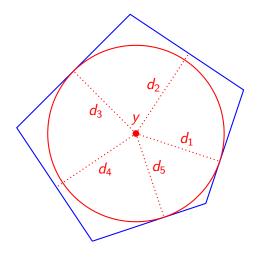


If *y* is the center, then draw perpendicular lines to each face of the polyhedron.

We want to maximize the smallest d_i . In other words,

$$\max_{y} \min_{i=1,\dots,5} \frac{d_i(y)}{d_i(y)}$$

The optimal *y* is the Chebyshev center

Finding the Chebyshev center amounts to solving an LP!



To compute the distance between y and the hyperplane $a^Tx = b$, notice that if the distance is r, then $y + \frac{r}{\|a\|}a$ belongs to the hyperplane:

$$a^{\mathsf{T}}\left(y+\frac{r}{\|a\|}a\right)=b$$

Simplifying, we obtain: $a^{T}y + ||a||r = b$

"The distance between y and each hyperplane is at least r" is equivalent to saying that $a_i^T y + ||a_i|| r \le b_i$ for each i.


Finding the Chebyshev center amounts to solving an LP!

The transformation to an LP is given by:

$$\max_{\substack{y \\ \text{s.t.}}} \min_{\substack{i=1,\ldots,k \\ a_i^{\mathsf{T}}y \leq b_i}} d_i(y) \implies \max_{\substack{y,r \\ \text{s.t.}}} r \\
\text{s.t.} \quad a_i^{\mathsf{T}}y + ||a_i||r \leq b_i \quad \forall i$$

Example: find the Chebyshev center of the polyhedron defined by the following inequalities:

$$2x - y + 2z \le 2$$
, $-x + 2y + 4z \le 16$, $x + 2y - 2z \le 8$, $x \ge 0$, $y \ge 0$, $z \ge 0$



Chebyshev.ipynb

Multi-period planning problems

- Optimization problems with a **temporal** component.
- Decisions must be made over the course of multiple time periods in order to optimize an overall cost.

Examples:

- scheduling: classes, tasks, employees, projects,...
- sequential decisions: investments, commitments,...

The decisions at each time period are **coupled** and must be jointly optimized. Otherwise we risk making decisions that seem good at the time but end up being very costly later.

Multi-period planning problems

- These problems tend to be tricky to model. It is often not clear what the decision variables should be.
- There are often more variables than you expect.

Important: Decision variables aren't always things that you decide directly!

We will see several examples of this...

Several tasks must be completed in order to build a house.

- Each task takes a known amount of time to complete.
- A task may depend on other tasks, and can only be started once those tasks are complete.
- Tasks may be worked on simultaneously as long as they don't depend on one another.
- How fast can the house be built?

Job No.	Description	Immediate predecessors	Normal time (days)
0	Start		0
Ь	Excavate and pour footers	o	4
c	Pour concrete foundation	Ь	2
d	Erect wooden frame including rough roof	c	4
•	Lay brickwork	d	6
f	Install basement drains and plumbing	c	1
g	Pour basement floor	f	2
h	Install rough plumbing	f	3
i	Install rough wiring	d	2
i	Install heating and ventilating	d,g	4
k	Fasten plaster board and plaster (including drying)	i,j,h	10
ı	Lay finish flooring	k	3
m	Install kitchen fixtures	1	1
n	Install finish plumbing	1	2
0	Finish corpentry	1	3
Р	Finish roofing and flashing	•	2
9	Fasten gutters and downspouts	P	1
r	Lay storm drains for rain water	c	1
5	Sand and varnish flooring	o,t	2
	Point	m,n	3
U	Finish electrical work	•	1
v	Finish grading	q,r	2
w	Pour walks and complete landscaping	•	5
	E1-1-L		


Source: HBR 1963

The data can be visualized using a directed graph.

 Arrows indicate task dependencies.

What are the decision variables?

- t_i : start time of i^{th} task.
- precedence constraints are expressed in terms of t_i's.
- minimize t_x .

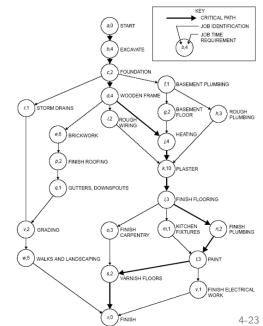


Source: HBR 1963

A small sample:

Let t_l , t_o , t_m , t_n , t_t , t_s be start times of the associated tasks.

Now use the graph to write the dependency constraints:



 Tasks o, m, and n can't start until task l is finished, and task l takes 3 days to finish. So the constraints are:

$$t_l + 3 \le t_o$$
, $t_l + 3 \le t_m$, $t_l + 3 \le t_n$

• Task t can't start until tasks m and n are finished. Therefore:

$$t_m+1\leq t_t, \quad t_n+2\leq t_t,$$

• Task s can't start until tasks o and t are finished. Therefore:

$$t_o + 3 \le t_s$$
, $t_t + 3 \le t_s$

Source: HBR 1963 4-24

Full implementation in Julia:

House.ipynb

Follow-up: which tasks in the project are **critical** to finishing on time? Which tasks can withstand delays?

related to notion of duality we will see later.
